


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	
1		NIB schedule.	1956 days	Fri 2/2/18	Fri 8/1/25		
2		Submit CON	1 day	Fri 2/2/18	Fri 2/2/18		
3		CON Review	44 wks	Mon 2/5/18	Fri 12/7/18	2	
4		Phase 1 Sitework and Parking Renovations Flat Lot	415 days	Mon 12/10/18	Fri 7/10/20		
5		Bid and Award Design	6 wks	Mon 12/10/18	Fri 1/18/19	3	
6		Design Flat Lot	16 wks	Mon 1/21/19	Fri 5/10/19	5	
7		Permitting	38 wks	Mon 5/13/19	Fri 1/31/20	6	
8		Bid and Award Construction	13 wks	Mon 9/9/19	Fri 12/6/19	6FS+17 wks	
9		Preconstruction	9 wks	Mon 12/9/19	Fri 2/7/20	8	
10		Construct Flat Lot	22 wks	Mon 2/10/20	Fri 7/10/20	7,9	
11		Phase 2 Inpatient Building, Garage, Power Plant	1320 days	Mon 12/10/18	Fri 12/29/23		
12		Inpatient Building and Garage	1320 days	Mon 12/10/18	Fri 12/29/23		
13		Bid and Award Design	12 wks	Mon 12/10/18	Fri 3/1/19	3	
14		Design Inpatient Building and Garage	70 wks	Mon 3/4/19	Fri 7/3/20	13	
15		Permitting	26 wks	Mon 7/6/20	Fri 1/1/21	14	
16		Bid and Award Construction	14 wks	Mon 7/6/20	Fri 10/9/20	14	
17		Preconstruction	9 wks	Mon 10/12/20	Fri 12/11/20	16	
18		Construct Inpatient Building and Garage	156 wks	Mon 1/4/21	Fri 12/29/23	15,10,17	
19		Power Plant	895 days	Mon 12/10/18	Fri 5/13/22		
20		Bid and Award Design	6 wks	Mon 12/10/18	Fri 1/18/19	3	
21		Design Power Plant	41 wks	Mon 1/21/19	Fri 11/1/19	20	
22		Permitting	8 wks	Mon 11/4/19	Fri 12/27/19	21	
23		Bid and Award Construction	8 wks	Mon 11/4/19	Fri 12/27/19	21	
24		Replace Chiller 1, 2 and Associated Infrastructure	52 wks	Mon 12/30/19	Fri 12/25/20	23	
25		Replace Replace Chiller 3 and Associated Infrastructure	36 wks	Mon 12/28/20	Fri 9/3/21	24	
26		Replace Chiller 4 and Associated Infrastructure	36 wks	Mon 9/6/21	Fri 5/13/22	25	
27		Phase 3 Furnish, Equip, Activate Clinical Building	435 days	Mon 10/3/22	Fri 5/31/24		
28		Procurement	18 wks	Mon 10/3/22	Fri 2/3/23	18FS-65 wks	
29		Preinstallation	13 wks	Mon 2/6/23	Fri 5/5/23	28	
30		Installation and Activation	56 wks	Mon 5/8/23	Fri 5/31/24	29	
31		Phase 4 Backfill Renovations and Activation	620 days	Mon 3/20/23	Fri 8/1/25		
32		Bid and Award Design	4 wks	Mon 3/20/23	Fri 4/14/23	30FS-63 wks	
33		Design Backfill Renovations	36 wks	Mon 4/17/23	Fri 12/22/23	32	
34		Permitting	6 wks	Mon 12/25/23	Fri 2/2/24	33	
35		Bid and Award Construction	6 wks	Mon 12/25/23	Fri 2/2/24	33	
36		Preconstruction	17 wks	Mon 2/5/24	Fri 5/31/24	35	
37		Construct/Activate Backfill Renovations	61 wks	Mon 6/3/24	Fri 8/1/25	34,36	

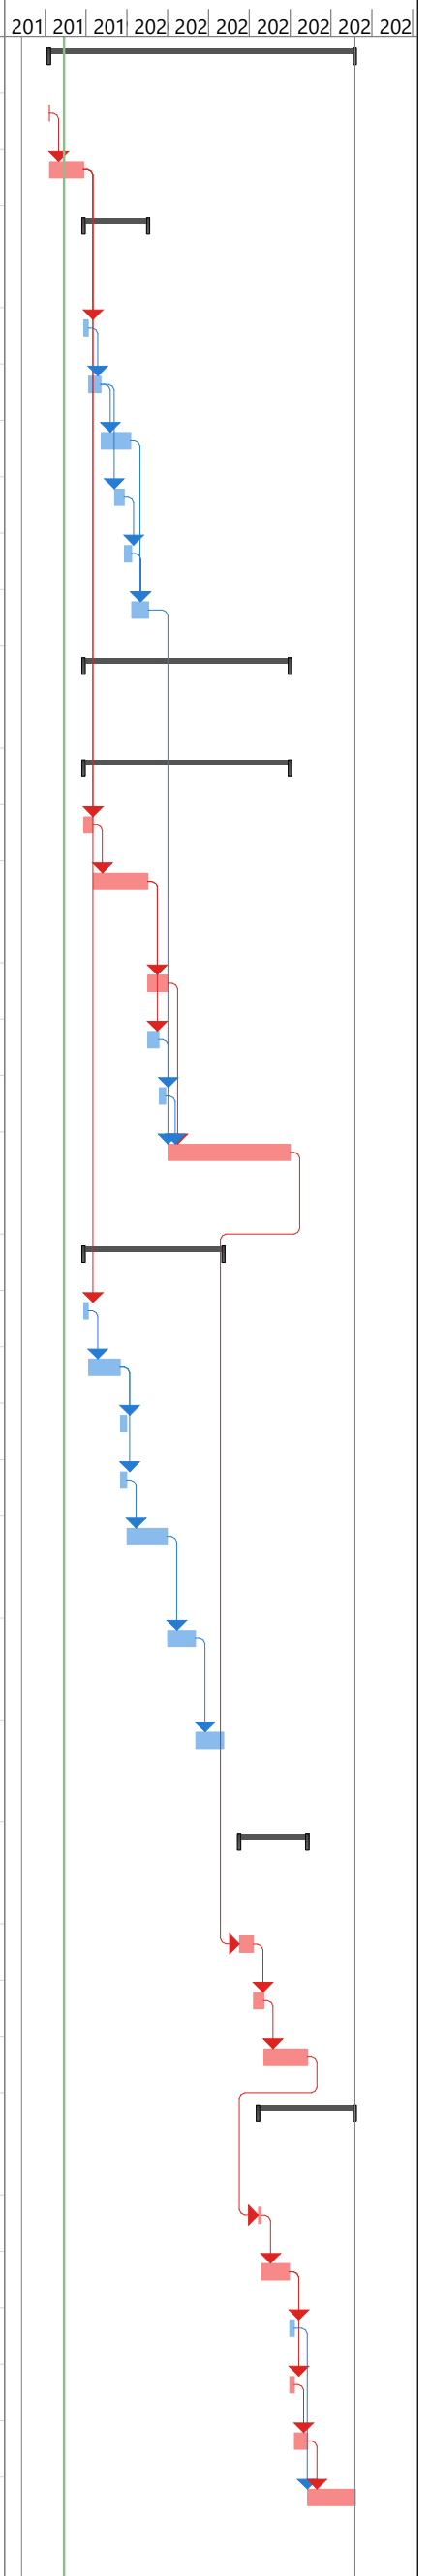

Project: schedule#1-6717(3) Date: Mon 6/18/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
